

Project Roadmap & Consolidated Patch Notes

Combines every patch-notes update, client fix log, and status report issued to date into one document.

PREPARED BY	PREPARED FOR	COVERS	LAST UPDATED
Aniket Gupta	Sheetal Ahuja · Totem Interactive	21 Aug – 3 Oct 2026	3 October 2026

Executive Summary

Reloved went from a blank repo to a live, publicly-used donation platform at **reloved.digital** in six weeks. The build ran in two halves:


- 21 Aug – 26 Sep: Product build-out and live Friends & Family testing.** Homepage, Wall of Kindness, Give/Claim flows, email + SMS notifications, privacy/handover logistics, AI photo processing, and real-user QA drove the bulk of the feature work and bug-fixing.
- 27 Sep – 3 Oct: Admin Control Center rebuild, security/scale hardening, multi-courier booking, and final feature polish.** The admin side was rebuilt into one operational surface backed by a production PostHog analytics integration; a security/concurrency audit closed race-condition and data-exposure gaps; Borzo/Shadowfax/Shiprocket booking was wired into Admin. The most recent ship (3 Oct) added donor-side instant schedule confirmation, widened the matching radius from 3km to 15km, and added FREE badges on item pages.

Live production site	reloved.digital (Firebase Hosting + Cloud Functions, asia-south1)
Core user journey	Donate → AI photo processing → publish to Wall → claim → courier pickup/delivery → confirmation — fully built, tested, and live
Admin Control Center	Rebuilt end-to-end; released 30 Sep with 28/28 UI tests, 32/32 live-safety tests, 65/65 backend tests passing
Tracked feature checklist	34 done · 2 in review · 1 not started
Biggest external blocker	Edesy call-masking automation and remaining MSG91 SMS template approvals — both sitting in third-party vendor queues

Nothing in this document is new work introduced here — every line ships from a dated commit or a client-facing note already sent. This document's job is to put the whole timeline, and what's left, in one place.

Development Timeline (Roadmap)

Seven working weeks, 21 Aug – 3 Oct 2026, plus the Phase 2 backlog. Solid bars are shipped and live; striped bars are in review; faded bars are not yet started.

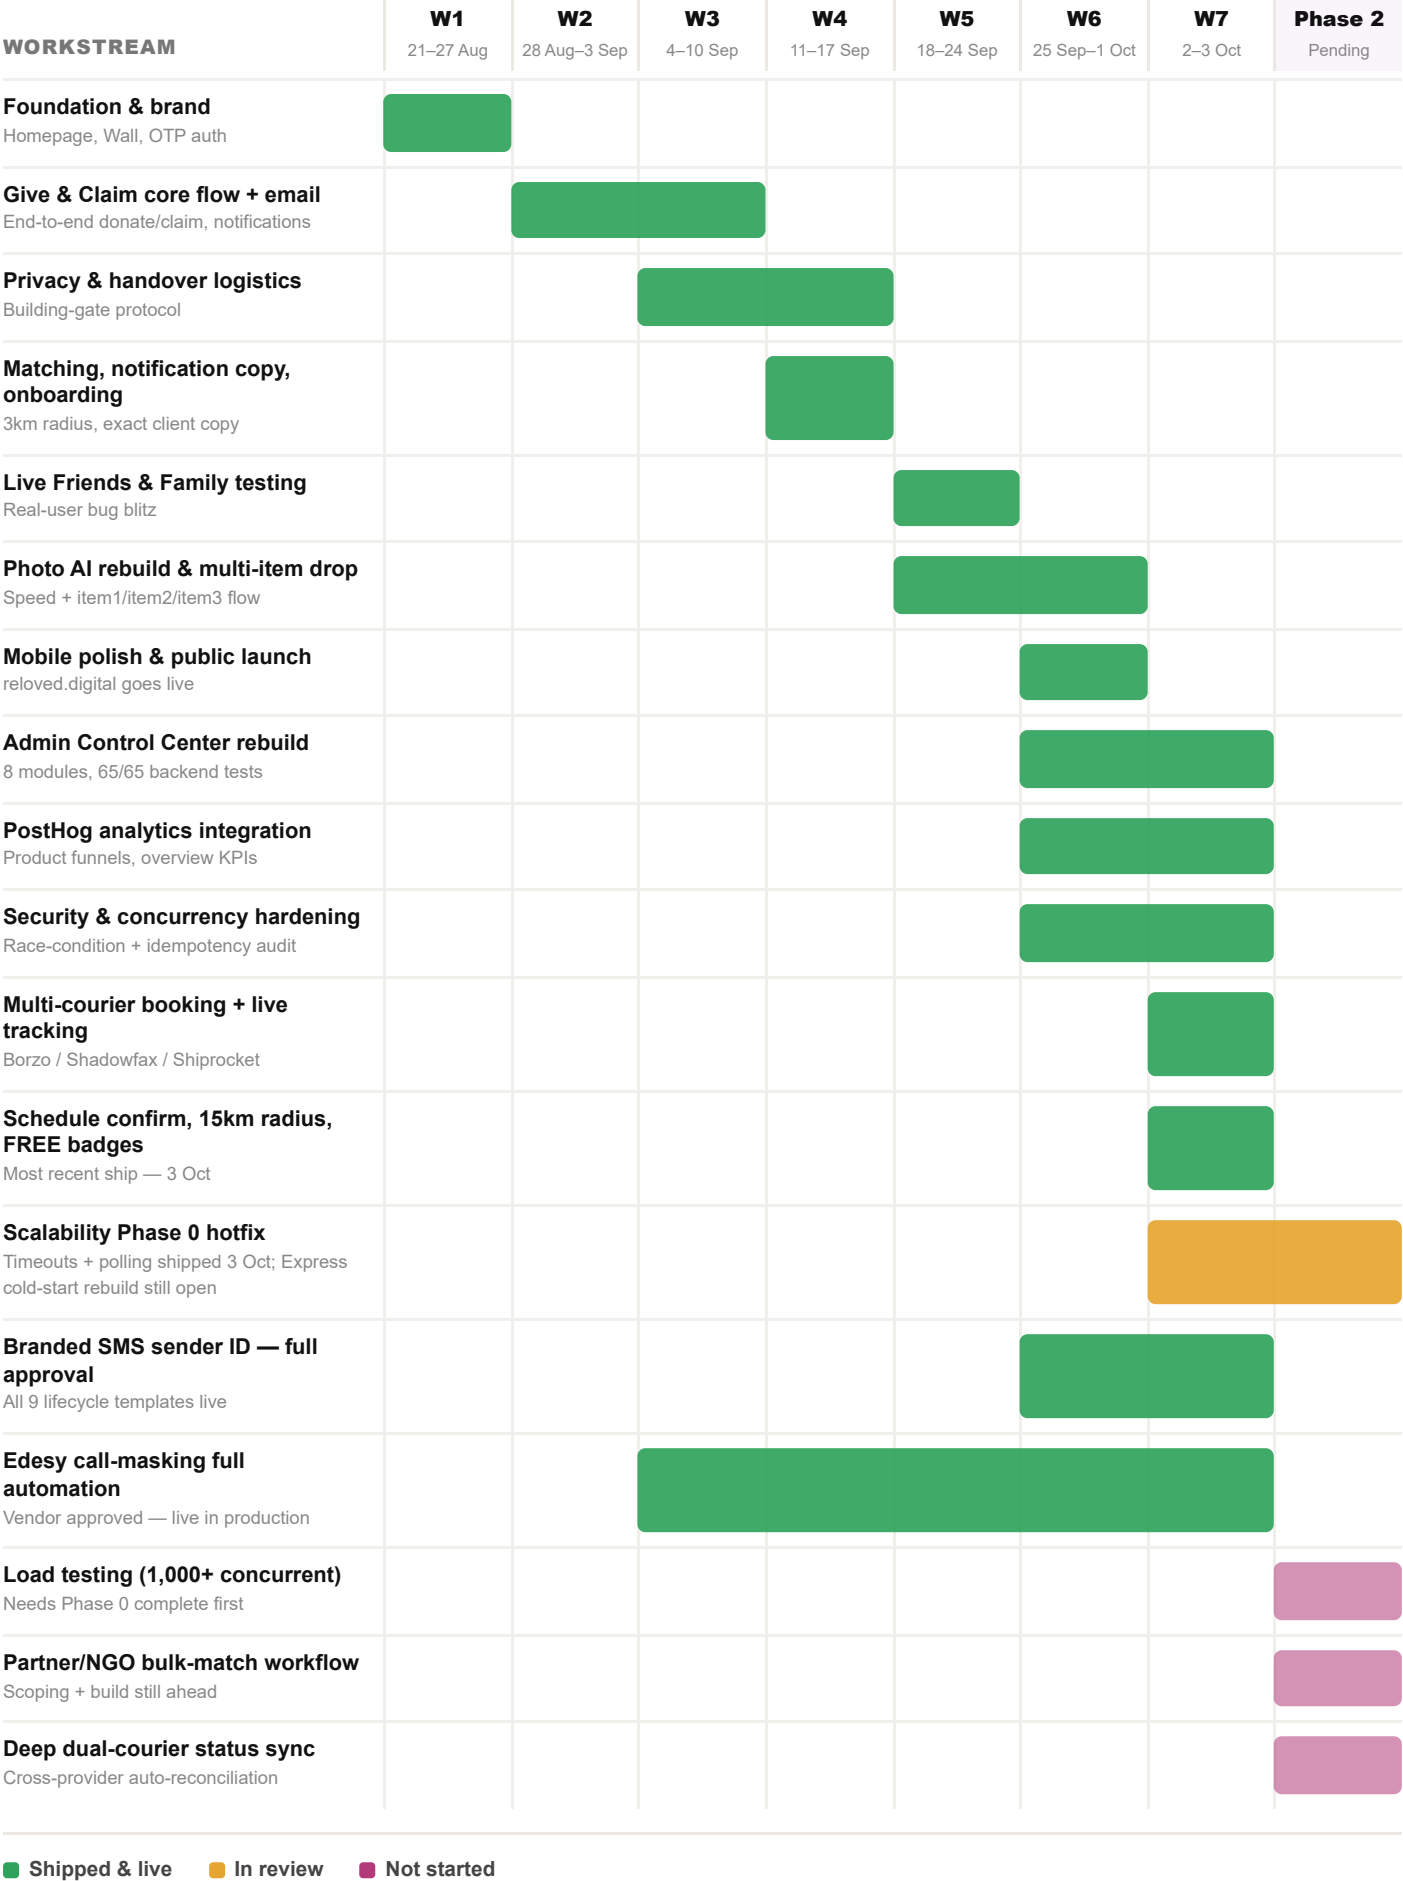

Phase-by-Phase Narrative

21 Aug – 26 Sep: Product build and live testing

Documented day-by-day with the exact client feedback behind each fix in `RELOVED_PATCH_NOTES.md`. Headlines: first version shipped by 29 Aug; first client feedback round 31 Aug; Privacy Policy and building-gate handoff protocol locked in by 10 Sep; Give/Claim/email flows connected end to end by 12 Sep; 3km matching and notification-copy rewrite by 16 Sep; live Friends & Family testing on 18–19 Sep produced the single largest batch of real-usage fixes in one evening; full site QA audit and public launch on `reloved.digital` by 24 Sep; Admin Overview and MSG91 SMS templates live by 26 Sep.

27 Sep – 3 Oct: Admin Control Center, security hardening, final feature push

27 Sep fixed live Drop/Claim breakage (storage bucket, a coordinate bug, grey-box Wall photos). 28–30 Sep ran two tracks in parallel: the Admin Control Center was rebuilt into one operational surface across 8 modules (released 30 Sep with 28/28 UI tests, 32/32 live-safety tests, 65/65 backend tests passing), while an independent security/concurrency audit closed race-condition and data-safety gaps, and a scalability plan was written for 1,000+ users. 1 Oct shipped Borzo/Shadowfax courier booking in Admin, fixed a misrouted-notification bug, and reworked the photo-AI pipeline. 2–3 Oct merged the Admin Control Center into the live handover branch and shipped donor instant schedule confirmation, a 15km matching radius (up from 3km), and FREE badges — the most recent release.

Pending Work / Phase 2 Roadmap

Nothing below blocks the platform from running day-to-day. This is what moves Reloved from “live and working” to “fully finished and scaled.”

ITEM	STATUS	WHY IT'S NOT DONE	BLOCKED ON
Scalability Phase 0 hotfix — full execution	IN REVIEW	Vendor-call timeouts (Brevo/MSG91/Borzo/Shadowfax/Shiprocket/Edesy/remove.bg), visibility-aware polling, and a warm instance (minInstances:1) shipped 3 Oct. Still open: the Express app still rebuilds on a cold lazy-import, and there's no IP rate limit yet on analyze/contact/login.	Engineering time
Load testing & 1,000+ concurrent-user verification	NOT STARTED	Needs Phase 0 hotfixes to land first, otherwise the test just measures known problems	Phase 0 completion
Direct-to-storage photo uploads	NOT STARTED	Uploads proxy through the function today; fine at current volume, a scale item for headroom	Engineering time
Deep dual-courier integration (auto status sync)	NOT STARTED	Deferred since 8–10 Sep so it didn't hold up launch; all three couriers are bookable from Admin today, cross-provider sync is not built	Scoping + engineering
Partner/NGO bulk-match workflow	NOT STARTED	NGOs can apply and be approved; matching a bulk donation to the right partner is a real feature, not a quick patch	Scoping + engineering
Defects picker, condition scale, liability waiver, photo guide	NOT STARTED	Good ideas from the 19 Sep deep-test session; need design thought	Design + engineering
Dashboard loading-state polish (all admin screens)	IN REVIEW	Shipped on the Wall; rollout to every dashboard screen is next	Engineering time
Donor dashboard data-fetch efficiency	IN REVIEW	Partially optimized; a further pass will cut repeated lookups	Engineering time

CLOSED OUT 3 OCT (EVENING)

FIXED & LIVE	Phone autofill on signup — Root cause was a missing `autoComplete` hint on the signup phone field; the Give form's equivalent field already had it and worked. Fixed on signup, the claim modal, contact/partner forms, and the account phone field.
FIXED & LIVE	Delivery/chat screen scoped to the active claim only — Confirmed each claim and donation has its own dedicated detail page and chat thread (/account/claims/:id, /account/gives/:id); re-verified against the rebuilt Admin Control Center's Claims/Deliveries views, which use the same single-record scoping.
FIXED & LIVE	Vendor-call timeouts + warm-instance cold start — Every vendor fetch that had no timeout now aborts instead of holding a function instance for the full 540s; one warm instance now absorbs cold starts. Most of the Scalability Phase 0 hotfix plan.
FIXED & LIVE	Edesy call-masking, full automation — Edesy approved the number and KYC; call masking is live in production.
FIXED & LIVE	Branded SMS sender ID, remaining DLT templates — MSG91/DLT carrier approved the remaining 4 templates (claim matched, delivery ready, schedule set, feedback thanks); all 9 lifecycle SMS templates are now live.

STILL HONESTLY OPEN — NOT RELABELED

NOT DONE	Dashboard loading-state polish / donor dashboard data-fetch efficiency — Open-ended UI and performance polish passes, not single fixable bugs — stay "in review" until actually finished.
NOT DONE	Load testing — Stays "not started" because no k6 run has actually been executed yet.

Full detail at every level of granularity lives in the companion documents: RELOVED_PATCH_NOTES.md (day-by-day), report.md (grouped by feature area), ReLoved_Status_Report.pdf (journey + pillars), and ADMIN_CONTROL_CENTER_RELEASE_NOTES.md (admin rebuild detail). This document is the single entry point that ties them together.
